


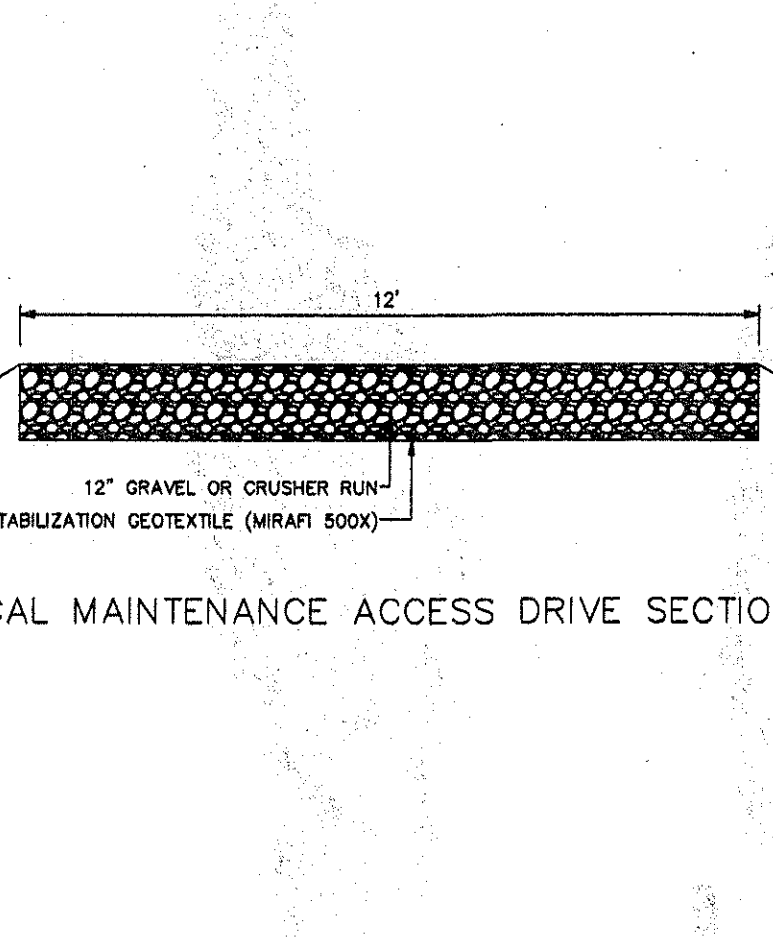
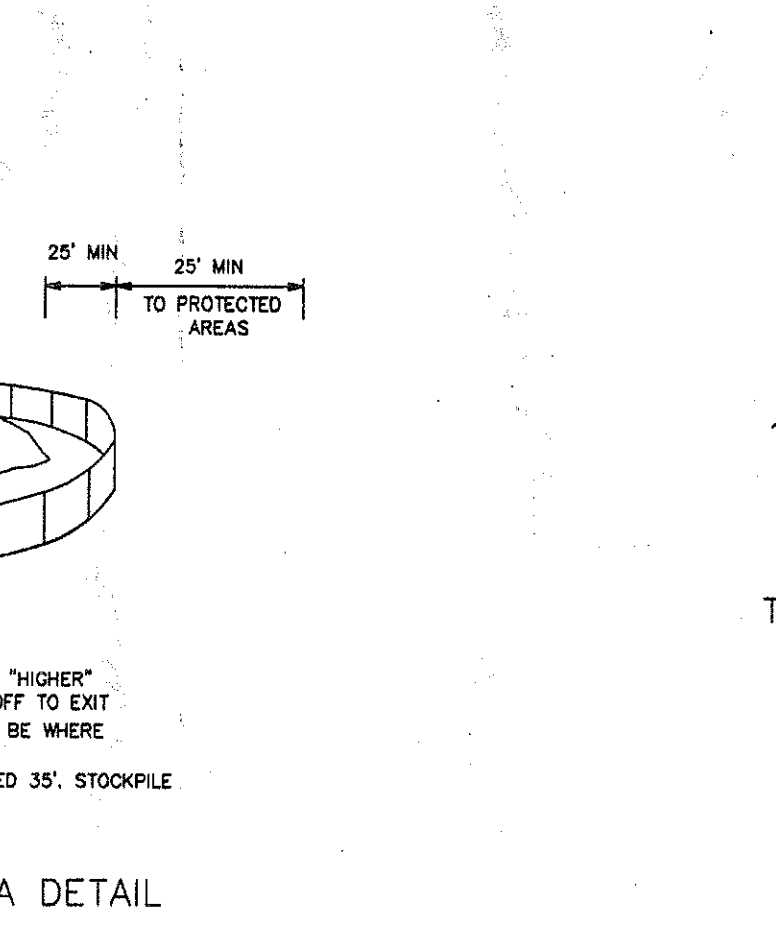
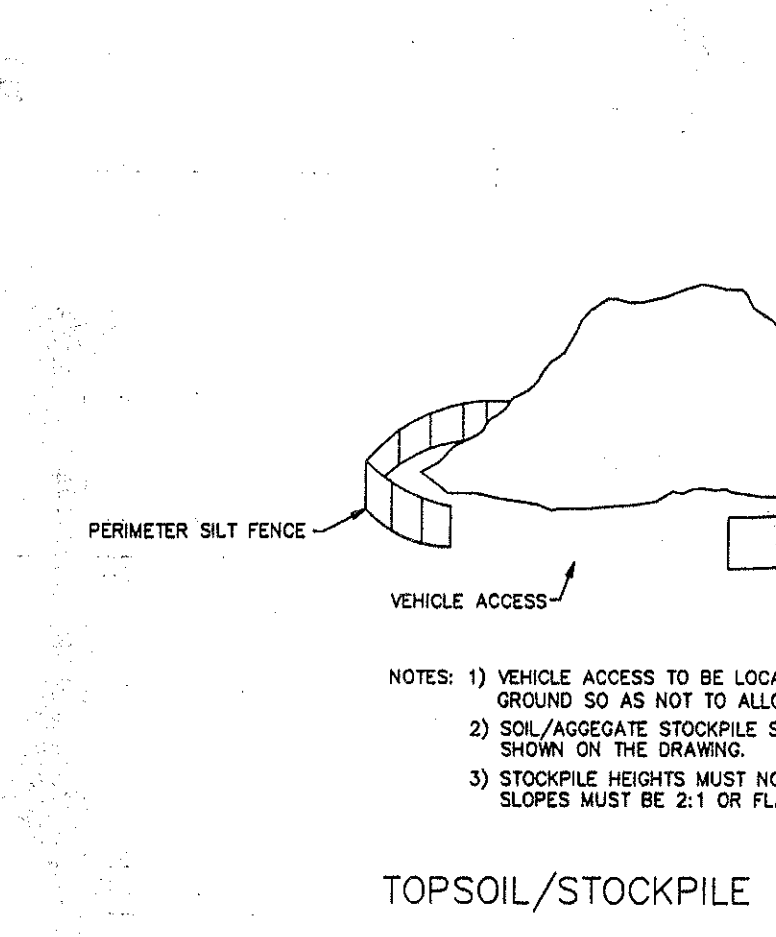
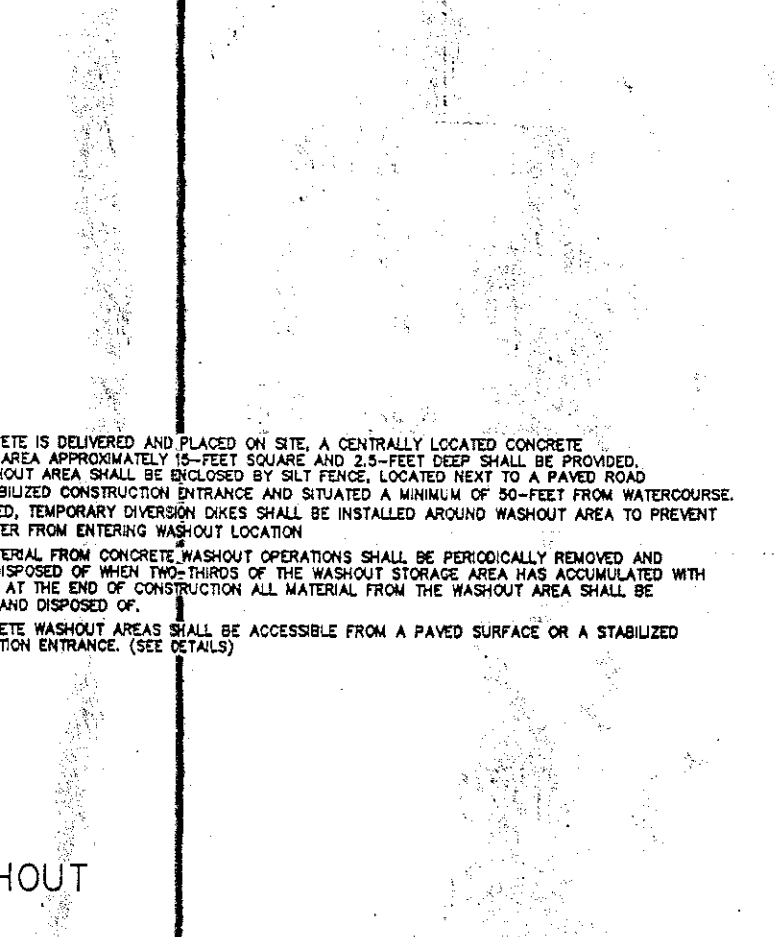
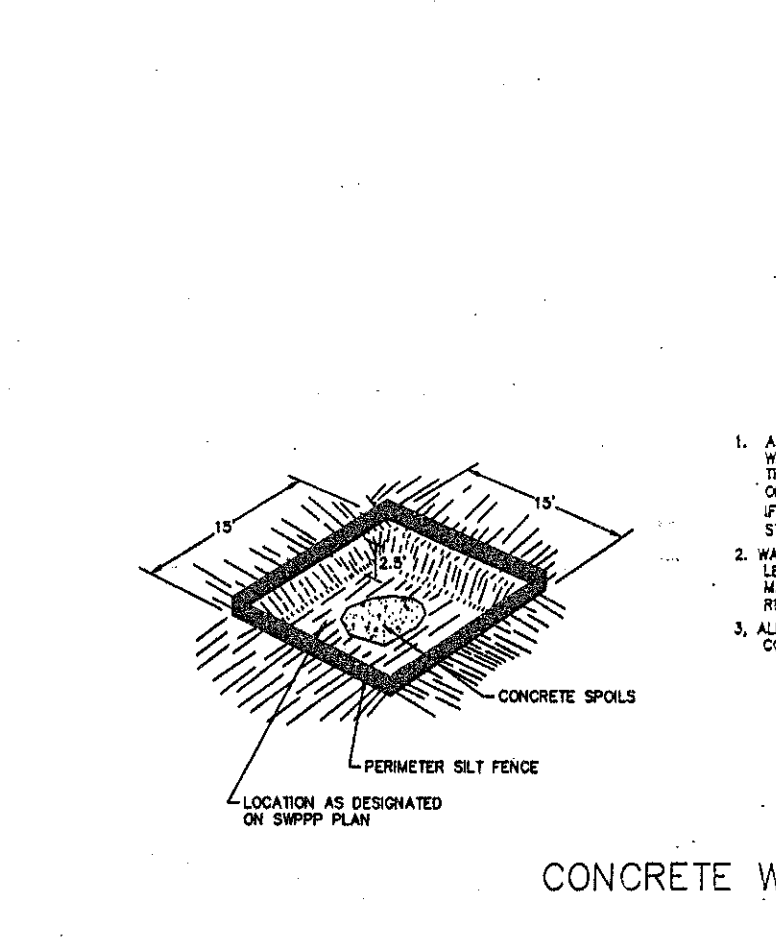
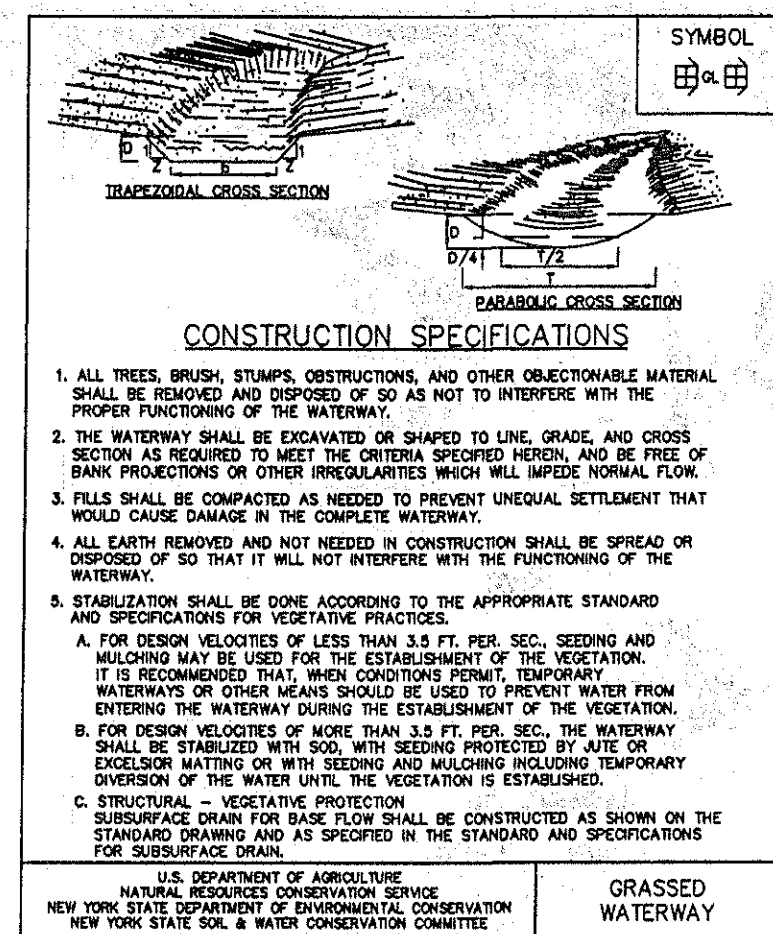
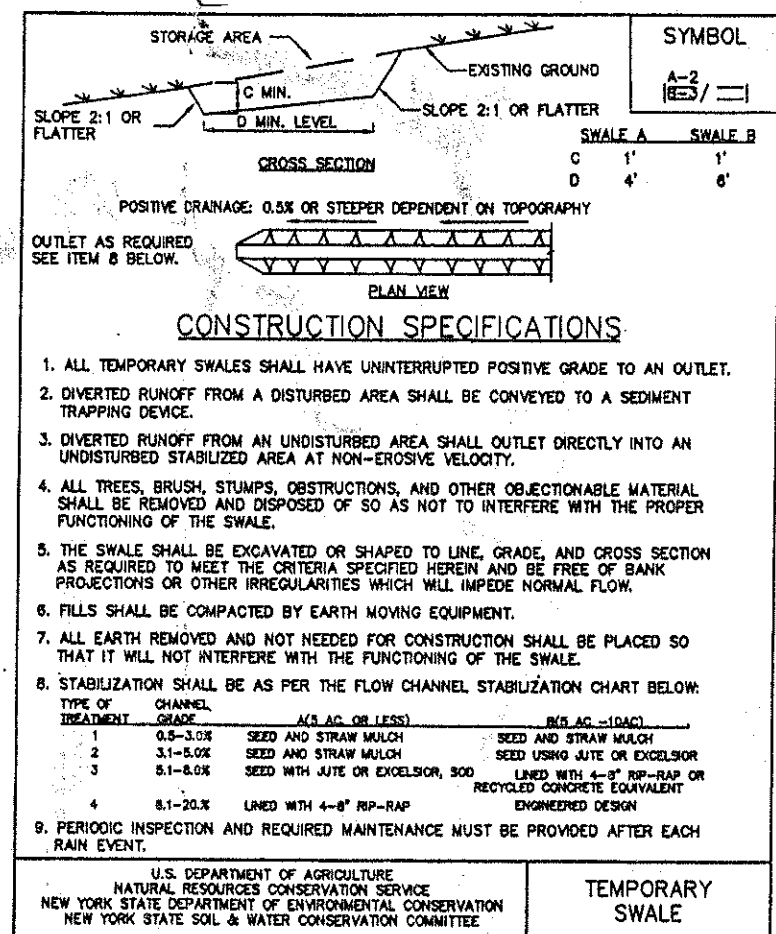
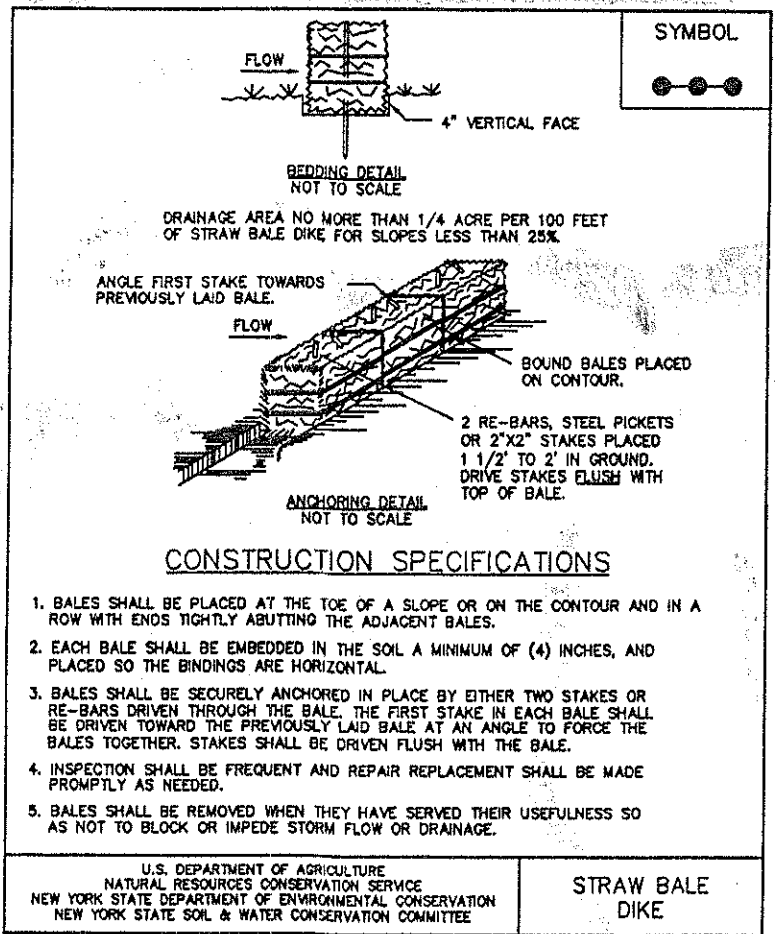
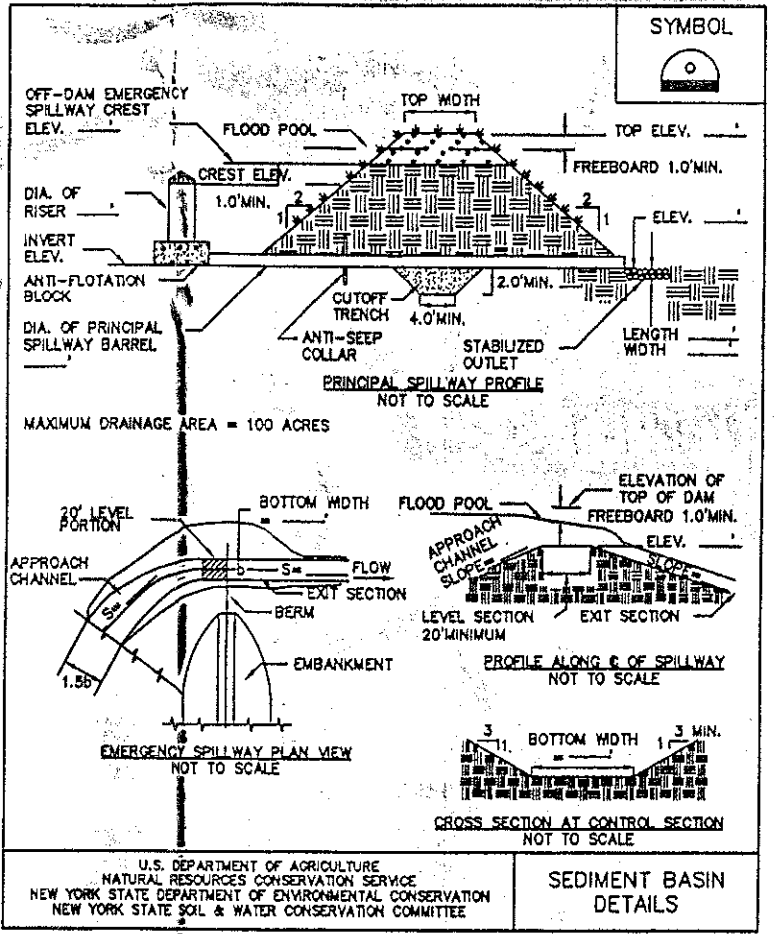
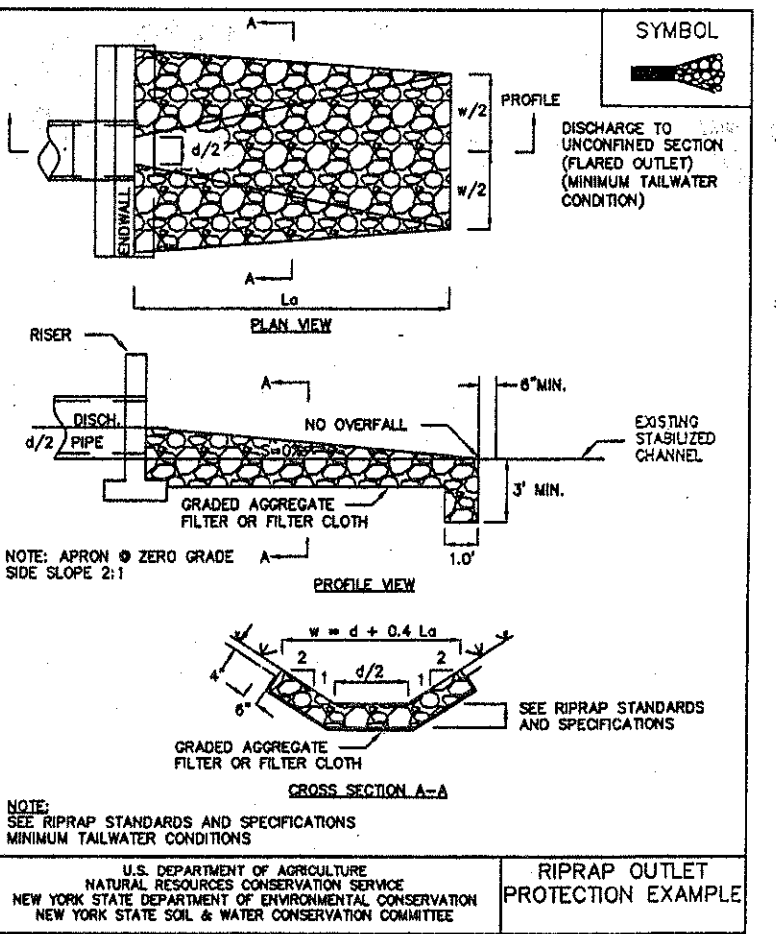
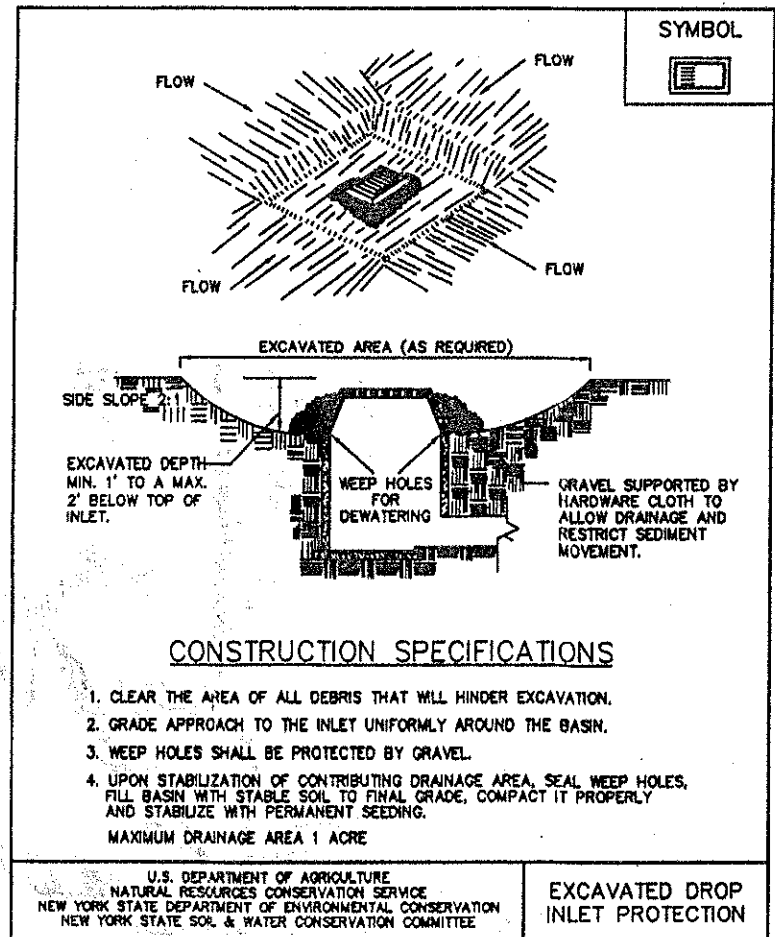
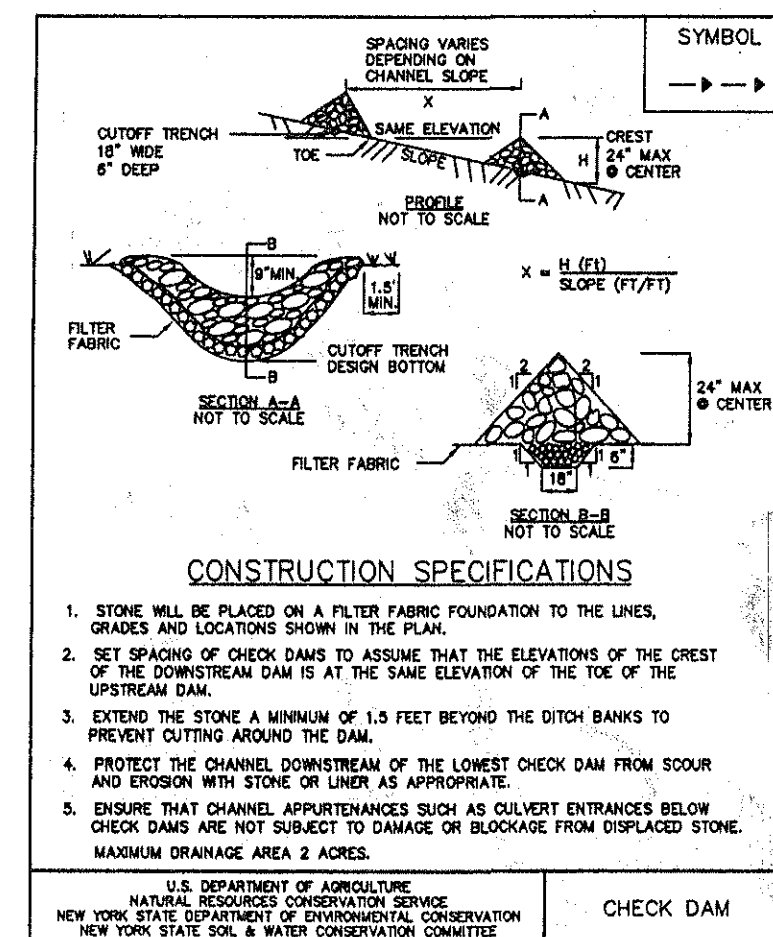
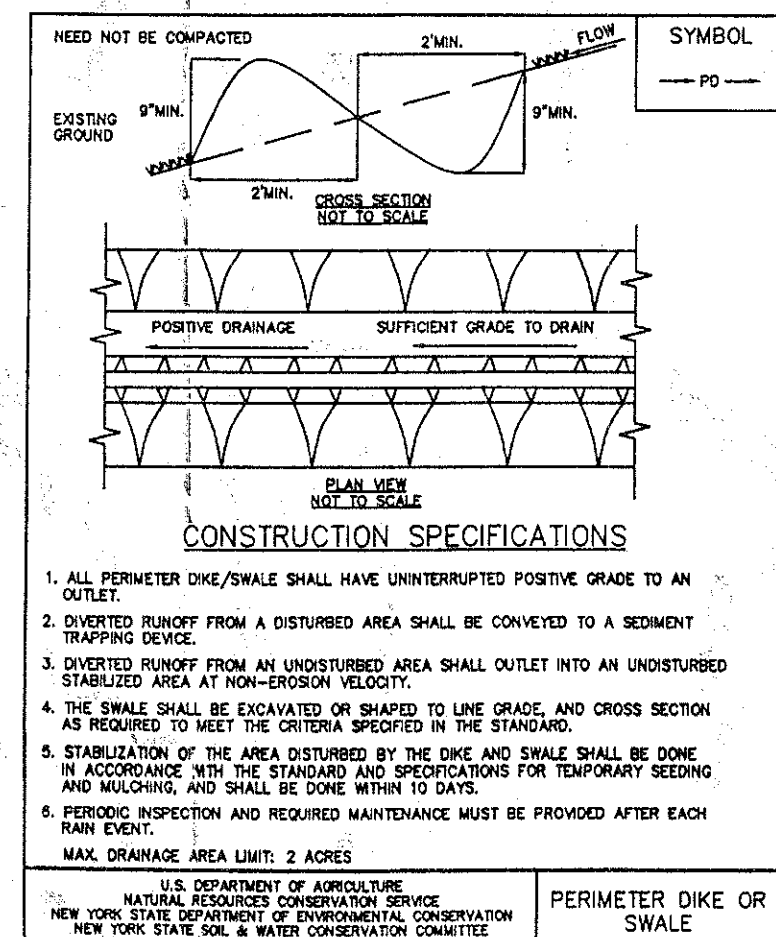
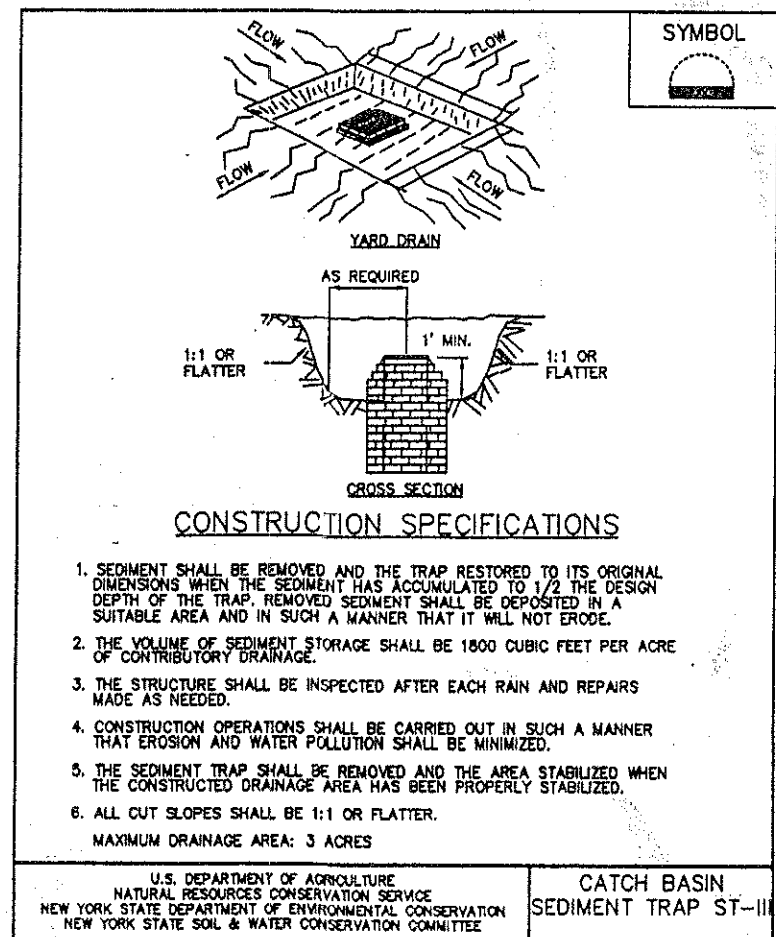
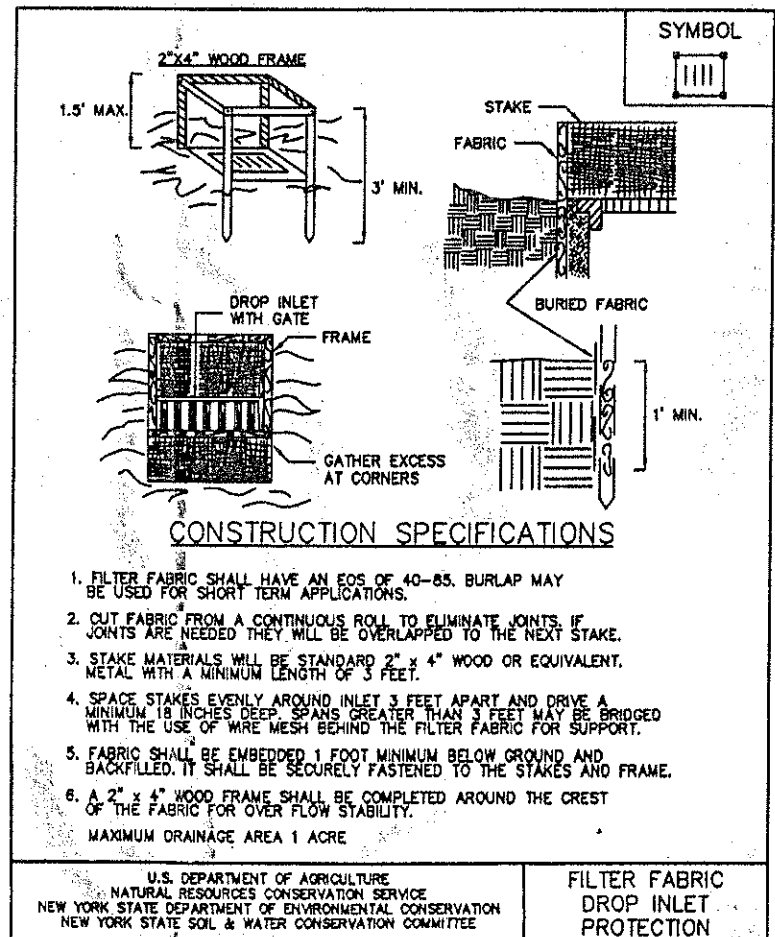
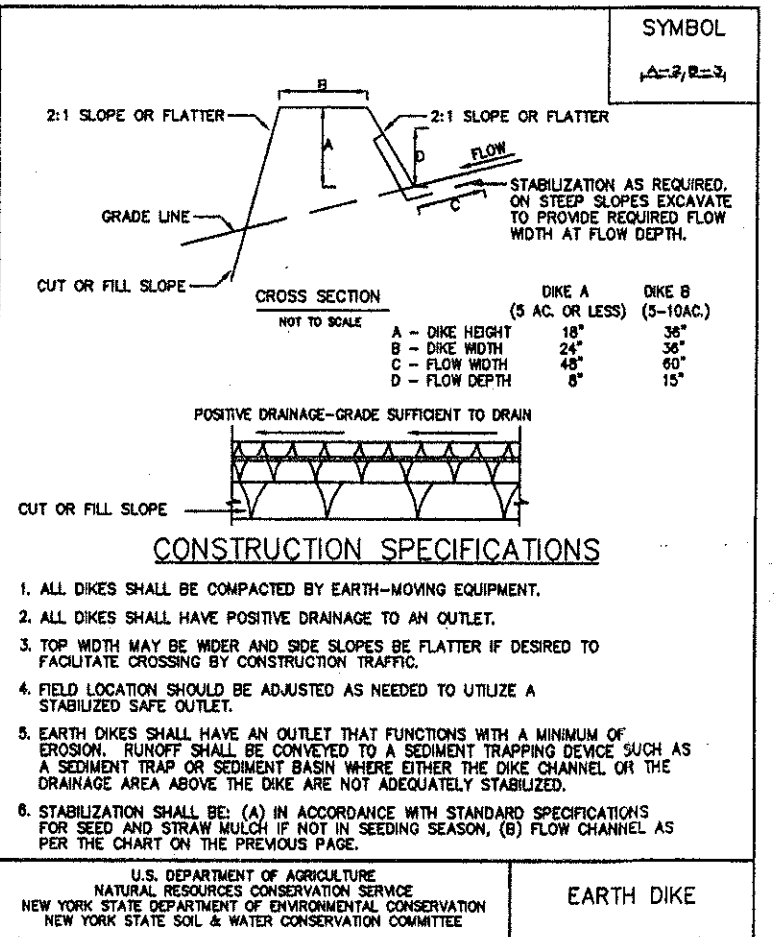
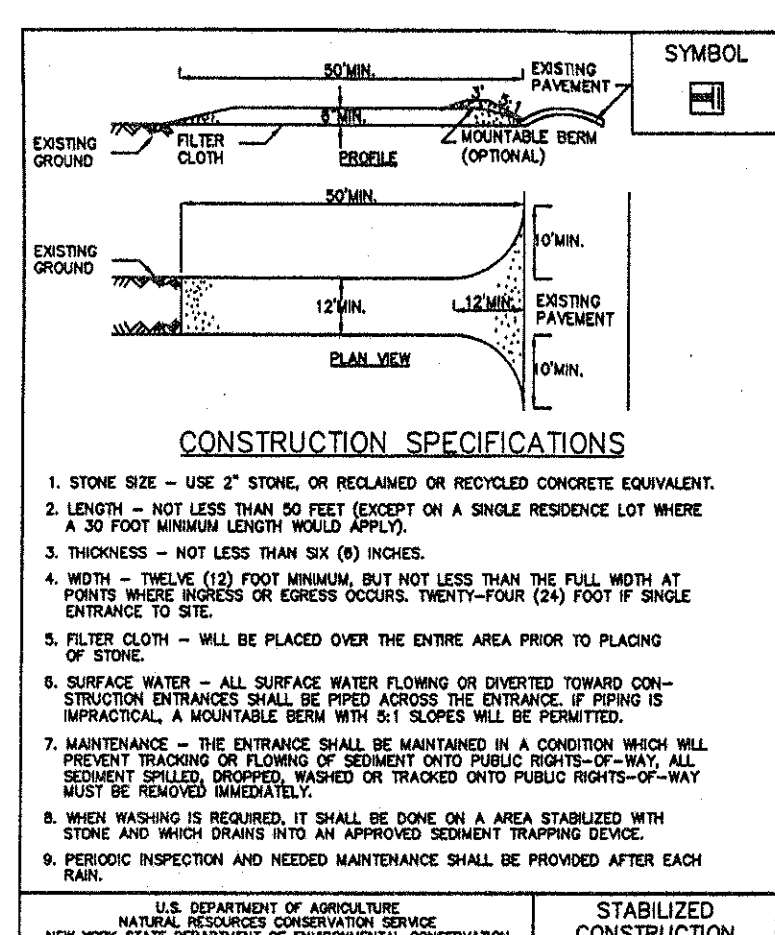
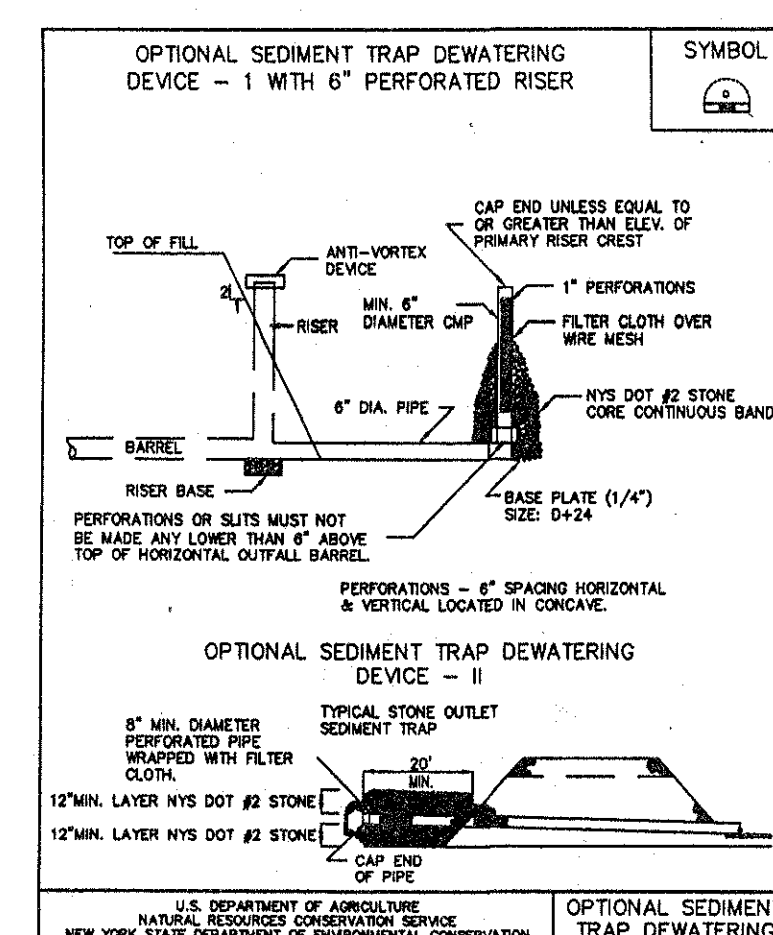
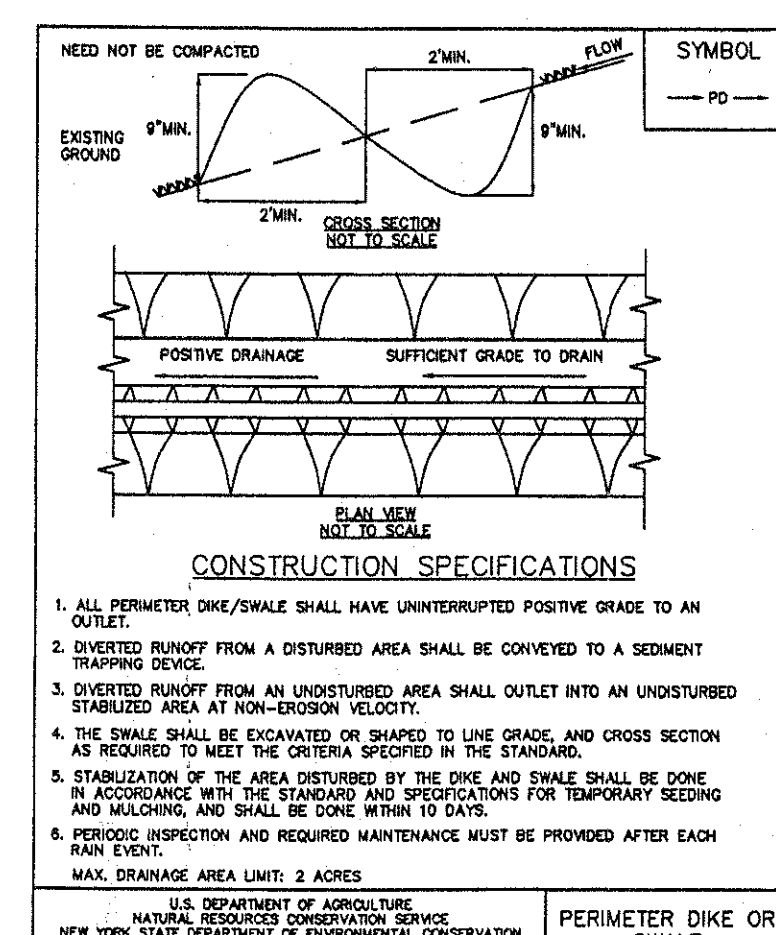
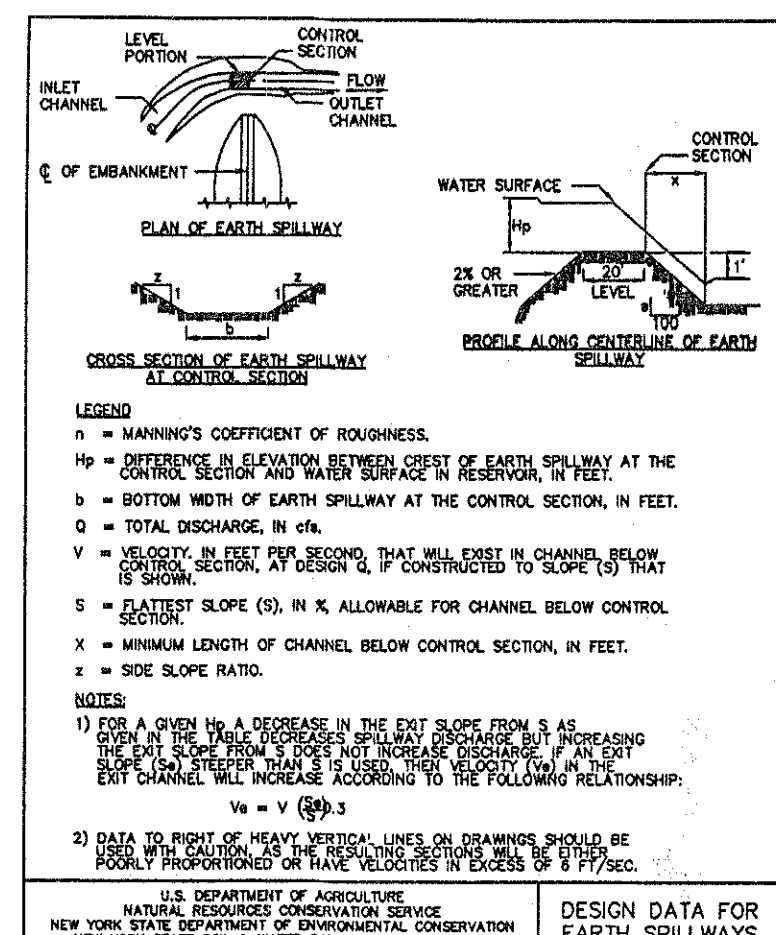


GENERAL NOTES:

1. ALL EROSION AND SEDIMENT CONTROL MEASURES SHALL ADHERE TO THE PROJECT'S STORMWATER POLLUTION PREVENTION PLAN (SWPPP). ALL APPROPRIATE STORMWATER CONTROL MEASURES NOTIFIED IN THE SWPPP SHALL BE IN PLACE BEFORE COMMENCING CONSTRUCTION OF ANY SEGMENT OF THE PROJECT THAT REQUIRES THESE MEASURES.
2. ALL EROSION AND SEDIMENT CONTROL MEASURES SHALL ADHERE TO THE SPECIFICATIONS AS STATED IN THE "NEW YORK STATE STANDARD SPECIFICATIONS FOR EROSION AND SEDIMENT CONTROL".
3. THE OWNER/OPERATOR SHALL HAVE A QUALIFIED PROFESSIONAL CONDUCT AN ASSESSMENT OF THE SITE PRIOR TO THE COMMENCEMENT OF CONSTRUCTION AND CERTIFY IN AN INSPECTION REPORT THAT THE APPROPRIATE EROSION AND SEDIMENT CONTROLS DESCRIBED IN THE SWPPP HAVE BEEN ADEQUATELY INSTALLED AND IMPLEMENTED TO ENSURE OVERALL PREPARATION OF THE SITE FOR THE COMMENCEMENT OF CONSTRUCTION. FOLLOWING THE COMMENCEMENT OF CONSTRUCTION, SITE INSPECTIONS SHALL BE CONDUCTED BY A QUALIFIED PROFESSIONAL AT LEAST ONCE EVERY SEVEN (7) CALENDAR DAYS TO ENSURE THE INTENSITY AND EFFECTIVENESS OF ALL EROSION AND SEDIMENT CONTROL PRACTICES.
4. THE OWNER/OPERATOR MUST MAINTAIN A RECORD OF ALL INSPECTION REPORTS IN A LOG BOOK THAT IS MAINTAINED ON SITE AND MADE AVAILABLE TO THE PERMITTING AUTHORITY UPON REQUEST.
5. THE OWNER/OPERATOR SHALL BE NOTIFIED BY A QUALIFIED INSPECTOR WITHIN ONE BUSINESS DAY OF ANY CORRECTIVE ACTIONS THAT NEED TO BE TAKEN. IMPLEMENTATION OF THE CORRECTIVE ACTION MUST COME WITHIN ONE BUSINESS DAY AFTER NOTIFICATION AND BE COMPLETED IN A REASONABLE TIME FRAME.
6. THE OWNER/OPERATOR SHALL BE NOTIFIED BY A QUALIFIED INSPECTOR WITHIN ONE BUSINESS DAY OF ANY CORRECTIVE ACTIONS THAT NEED TO BE TAKEN. IMPLEMENTATION OF THE CORRECTIVE ACTION MUST COME WITHIN ONE BUSINESS DAY AFTER NOTIFICATION AND BE COMPLETED IN A REASONABLE TIME FRAME.
7. THE CONTRACTOR SHALL INITIATE STABILIZATION MEASURES AS SOON AS PRACTICABLE ON PORTIONS OF THE SITE WHERE CONSTRUCTION ACTIVITIES HAVE TEMPORARILY OR PERMANENTLY CEASED.
8. TEMPORARY CONSTRUCTION SILT FENCES SHALL BE PLACED ON CONTOURS WHERE THERE IS NO CONCENTRATION OF STORMWATER RUNOFF FLOWING TO AND WHERE EROSION OCCURS IN THE FORM OF SHEET EROSION. SEE DETAIL. SILT FENCES SHALL BE UNDISTURBED AND UNCAVATED AREA.
9. LIMITS OF CLEARING AND DISTURBANCE SHALL BE CLEARLY MARKED AND REMAIN SO THROUGHOUT THE DURATION OF CONSTRUCTION ACTIVITIES.
10. CLEARING AND EXCAVATING ACTIVITIES SHALL BE CONDUCTED IN SUCH A MANNER AS TO MAINTAIN VEGETATIVE COVER AS MUCH AS PRACTICABLE.
11. WHEN CONSTRUCTION ACTIVITIES CEASE, SOIL STOCKPILES AND EXPOSED SOIL SHALL BE STABILIZED BY SEED, MULCH OR OTHER APPROPRIATE MEASURES AS SOON AS POSSIBLE. IN NO CASE SHALL THESE SOILS AND STOCKPILES REMAIN UNSTABILIZED FOR MORE THAN 14 DAYS AFTER CONSTRUCTION ACTIVITIES HAVE CEASED. PERMANENT STABILIZATION SHALL BE INSTALLED IMMEDIATELY FOLLOWING FINAL GRADING.
12. NO FILLING, GRADING OR OTHER DISTURBANCE INCLUDING SILT IS ALLOWED IN EXISTING DRAINAGE CHANNELS UNLESS INDICATED ON GRADING PLAN.

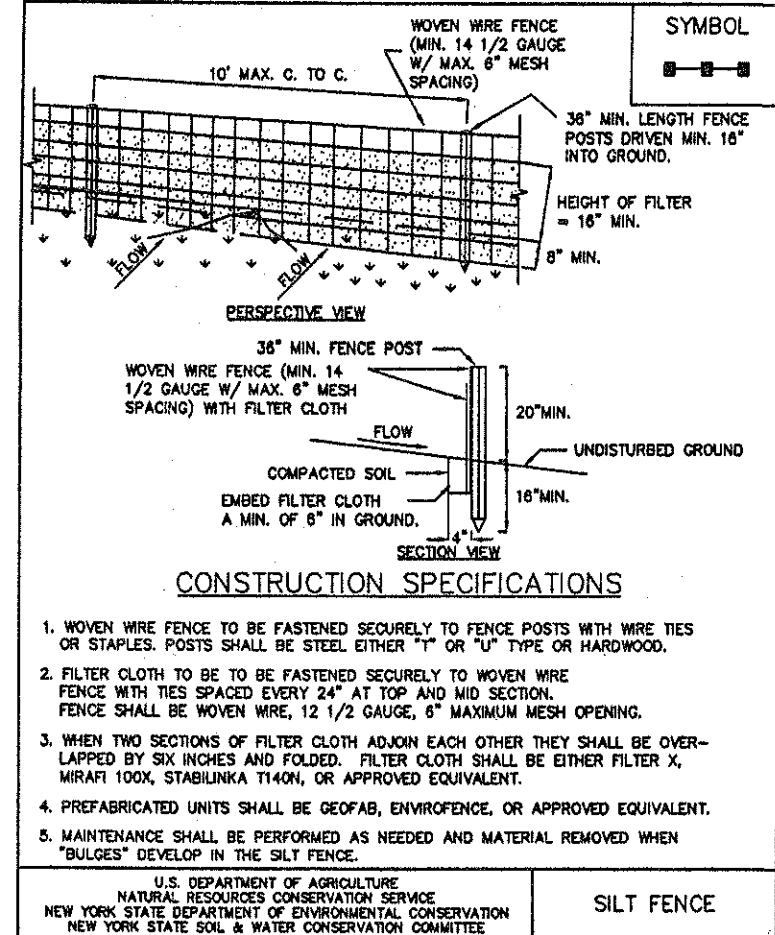

DATE	BY	SCALE	REVISION
02/15/14	RTT	1" = 10'	1

VAN DYKE SPINNEY
PHASE 2
 TOWN OF BETHEHEM
 COUNTY OF ALBANY
 STATE OF NEW YORK

TOWN OF BETHEHEM
 PLANNING BOARD
 TOWN OF BETHEHEM
 ALBANY COUNTY, NEW YORK
 By direction of the Chairman,
 These drawings are hereby approved.
 See sheet(s) 13 of 23
 for date and signature.

BREWER ENGINEERING ASSOCIATES, P.C.
 CONSULTING ENGINEERS - PLANNERS
 743 COLUMBIA TURNPIKE, EAST GREENBUSH, NEW YORK 12061
 PHONE: 518-477-5233 FAX: 518-477-5233
